

# NOTICE OF INTENT TO COMMENCE CONSTRUCTION - UPDATE

May 21, 2012


This update to the notice of intent to commence construction is provided by Ocotillo Express LLC, in compliance with the requirements of the Agreement to Implement Health, Safety, Environmental and Related Measures for the Ocotillo Wind Energy Facility on Certain BLM-Administered Federal Lands Within the County of Imperial (Implementation Agreement).

**PLEASE BE ADVISED THAT THE BLM RECORD OF DECISION, RIGHT OF WAY GRANT AND NOTICE TO PROCEED HAVE BEEN ISSUED FOR THIS PROJECT AS OF MONDAY, MAY 14, 2012, AND CONSTRUCTION COMMENCED ON MAY 15, 2012.**


In addition to the work described on the original Notice of Intent to Commence Construction provided by Ocotillo Express LLC, which includes clearing and grading of the project laydown yard, substation access road and substation area (refer to areas indicated in pink on the map below), work will also occur on the area shown in blue on the map below. All work will be done in accordance with permit requirements and restrictions. During the first month of construction, work will primarily focus on the substation area as well as geotechnical investigations of the turbine sites.

On the reverse side of this Notice, an updated construction schedule is provided. If you observe significant undesirable noise conditions associated with construction, you may report the matter by calling (760) 890-8663.

Ocotillo Express LLC intends to continue to be a good neighbor and will attempt to minimize disruptions caused by our construction activities.

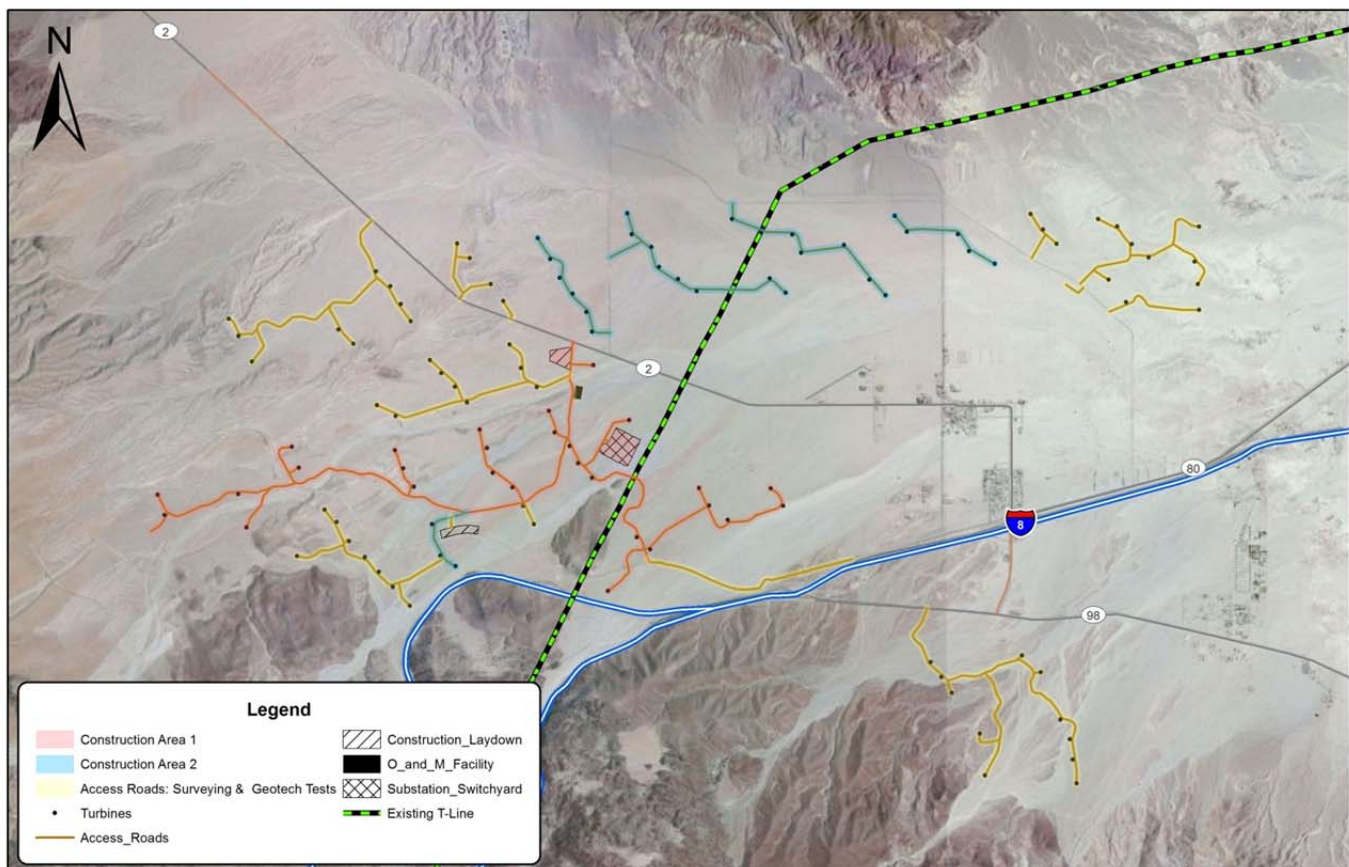

**Ocotillo Wind Project**  
**Imperial County, California**



## Ocotillo Wind Project - Proposed Construction Schedule

<b>Task Name</b>	<b>Start</b>	<b>Finish</b>
Notice to Proceed (actual)	Monday, May 14, 2012	
Start of Substation Construction (including access)	Wednesday, May 16, 2012	Friday, November 30, 2012
Start of Laydown Area Construction	Tuesday, May 15, 2012	Friday, June 01, 2012
Start of Geotechnical Investigation	Thursday, May 17, 2012	Friday, July 20, 2012
Start of Road and Turbine Site Construction	Monday, May 21, 2012	Monday, July 30, 2012
Start Operations & Maintenance Facility Construction	Monday, June 18, 2012	Thursday, January 24, 2013
Start of Turbine Foundation Work	Monday, June 25, 2012	Wednesday, October 03, 2012
Start of Turbine Deliveries 2012 (average 6/week)	Wednesday, August 08, 2012	Wednesday, November 14, 2012
Turbine Installation - (2012)	Monday, August 13, 2012	Tuesday, November 20, 2012
Underground Collection System Construction	Tuesday, July 10, 2012	Tuesday, January 15, 2013
Permanent Met Tower Installations	Friday, August 03, 2012	Tuesday, October 30, 2012
SDG&E and Ocotillo Substations Energized	Friday, November 30, 2012	
Substantial Completion – 2012 Installation	Friday, December 07, 2012	
Start of Turbine Deliveries 2013 (average 6/week)	Wednesday, February 06, 2013	Tuesday, March 19, 2013
Turbine Installation - (2013)	Wednesday, February 13, 2013	Friday, April 12, 2013
Substantial Completion – 2013 Installation	Tuesday, May 01, 2012	
Restoration/ completion and maintenance of revegetation	Monday, December 03, 2012	Tuesday, December 31, 2013
